
Burndown

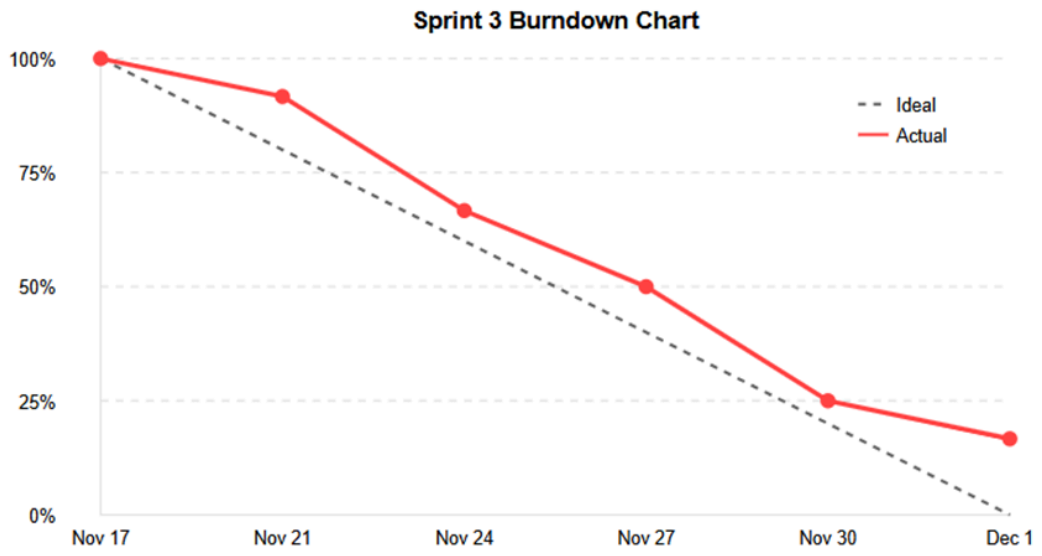

Planned Velocity

We had hoped to get the backend to frontend functionality quickly, expecting it to take 1-3 days to make sure it works properly. Otherwise, we wouldn't be able to interface between the two to test functionality.

The Trello points we set were mostly final touches as we expected to be done most of the other necessary functions within the first week. We expected to be able to implement extra features such as foreign currency accounts, and viewing currency exchange rates. This would be done after all basic functionality (withdraw, deposit, transfers) has already been created.

Sprint Velocity

The connection between frontend to backend through http requests proved more difficult than we initially thought, slowing down development. To solve this, we moved from using plain Java to using the Spring framework. In addition, some group members had trouble with git and GitHub, so we had to use other file transfer options to share our changes. Lastly, we tried to add the potential for multiple accounts per user, but we kept running into problems. In the end, we ran out of time and had to scrap the idea.
